



# Cardiff Heat Network Ltd

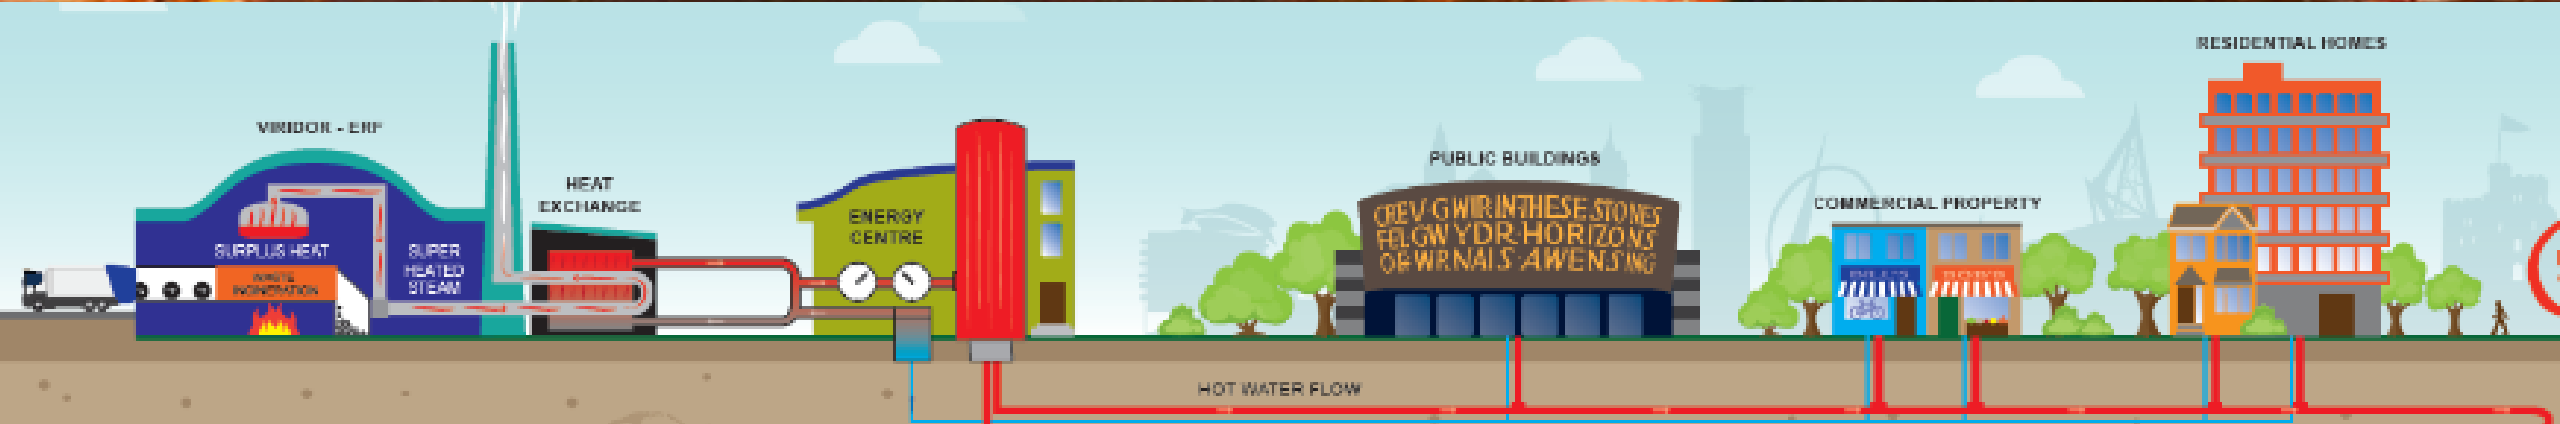

# Cardiff Heat Network: Phase 1

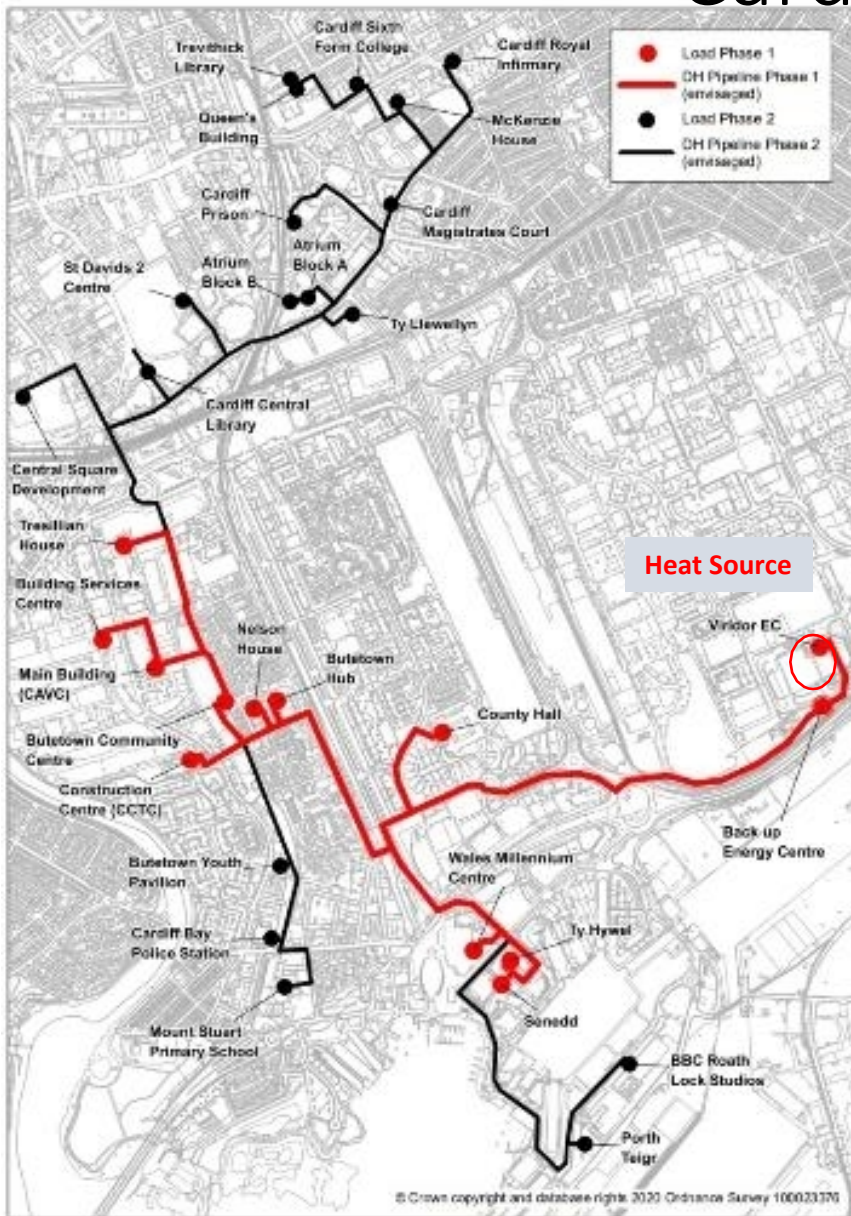


- Phase 1 fully funded – Welsh Govt Loan and HNIP Grant (£15m)
- Heat Source – existing ERF (Viridor)
- 15 MW peak heat available
- Public Sector customer base to underpin early business case
- Positively received Nationally and Locally – major win for the City
- DBOM Contractor procured – HEMIKO (Pinnacle Power)
- On site - Successful rollout
  - Energy centre near completion
  - Substantial pipe infrastructure installed
  - Internal works at 2 anchor customers complete
  - Approx £8m spend to date
- Completion summer 24



Working for Cardiff, working together

# Cardiff Heat Network Project Progress – Oct 23

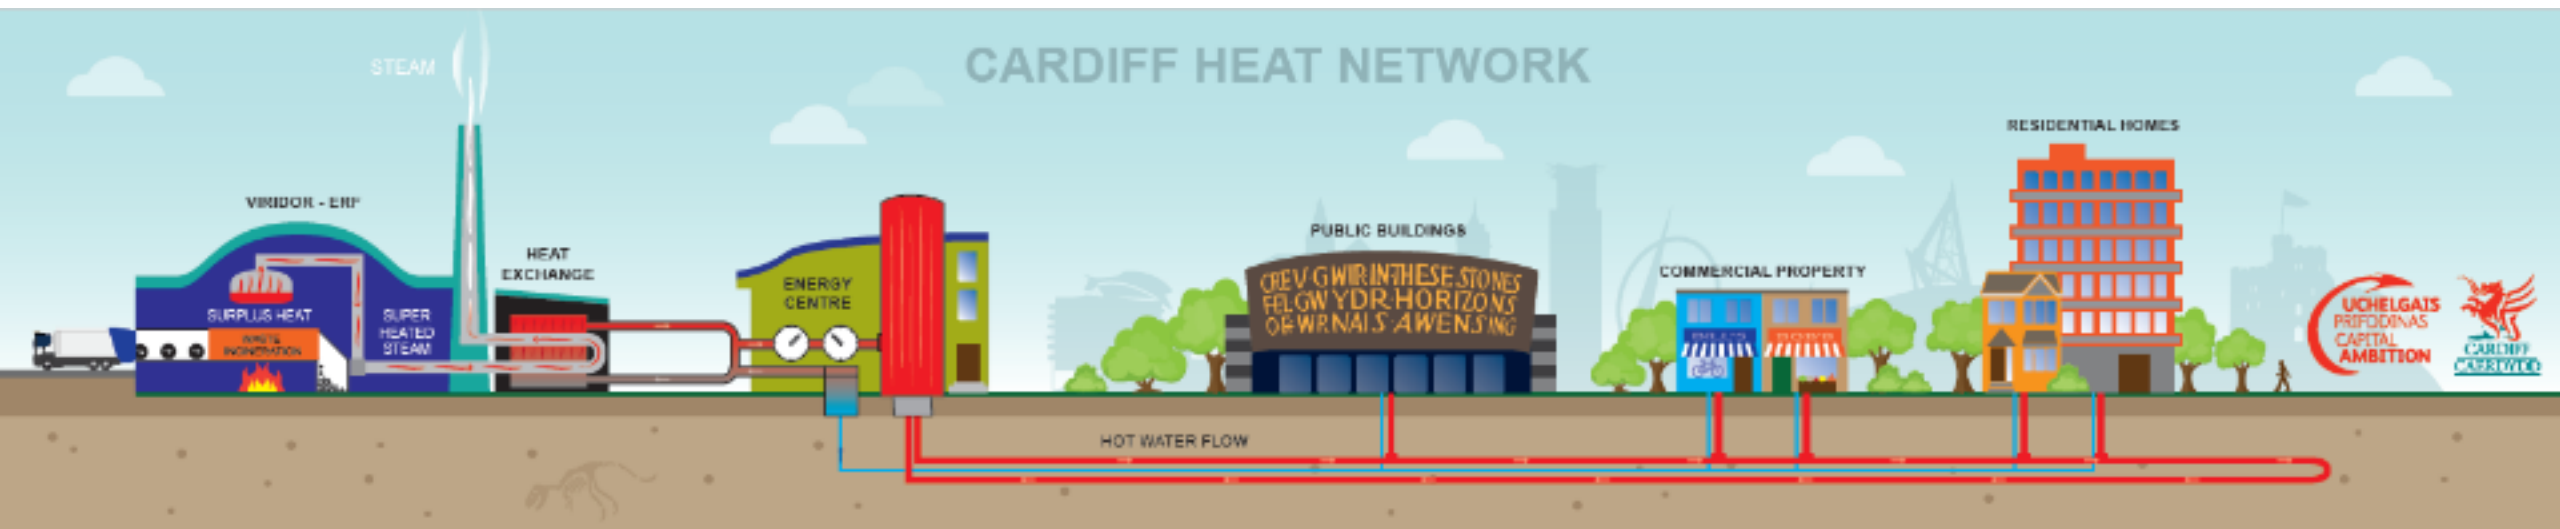

Gweithio dros Gaerdydd, gweithio gyda'n gilydd  
Working for Cardiff, working together


# Progress on Site – Oct 23



## Energy Centre Construction



## Network Installations

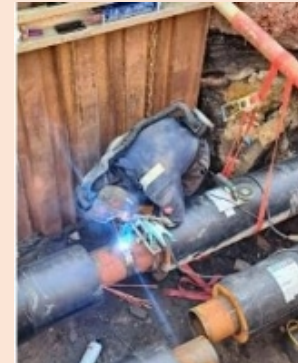

## First Customer Connections (WMC)



Gweithio dros Gaerdydd, gweithio gyda'n gilydd  
Working for Cardiff, working together




# Progress on Site: Senedd/Ty Hywel Connection



Gweithio dros Gaerdydd, gweithio gyda'n gilydd  
Working for Cardiff, working together



# Progress on Site – Oct 23

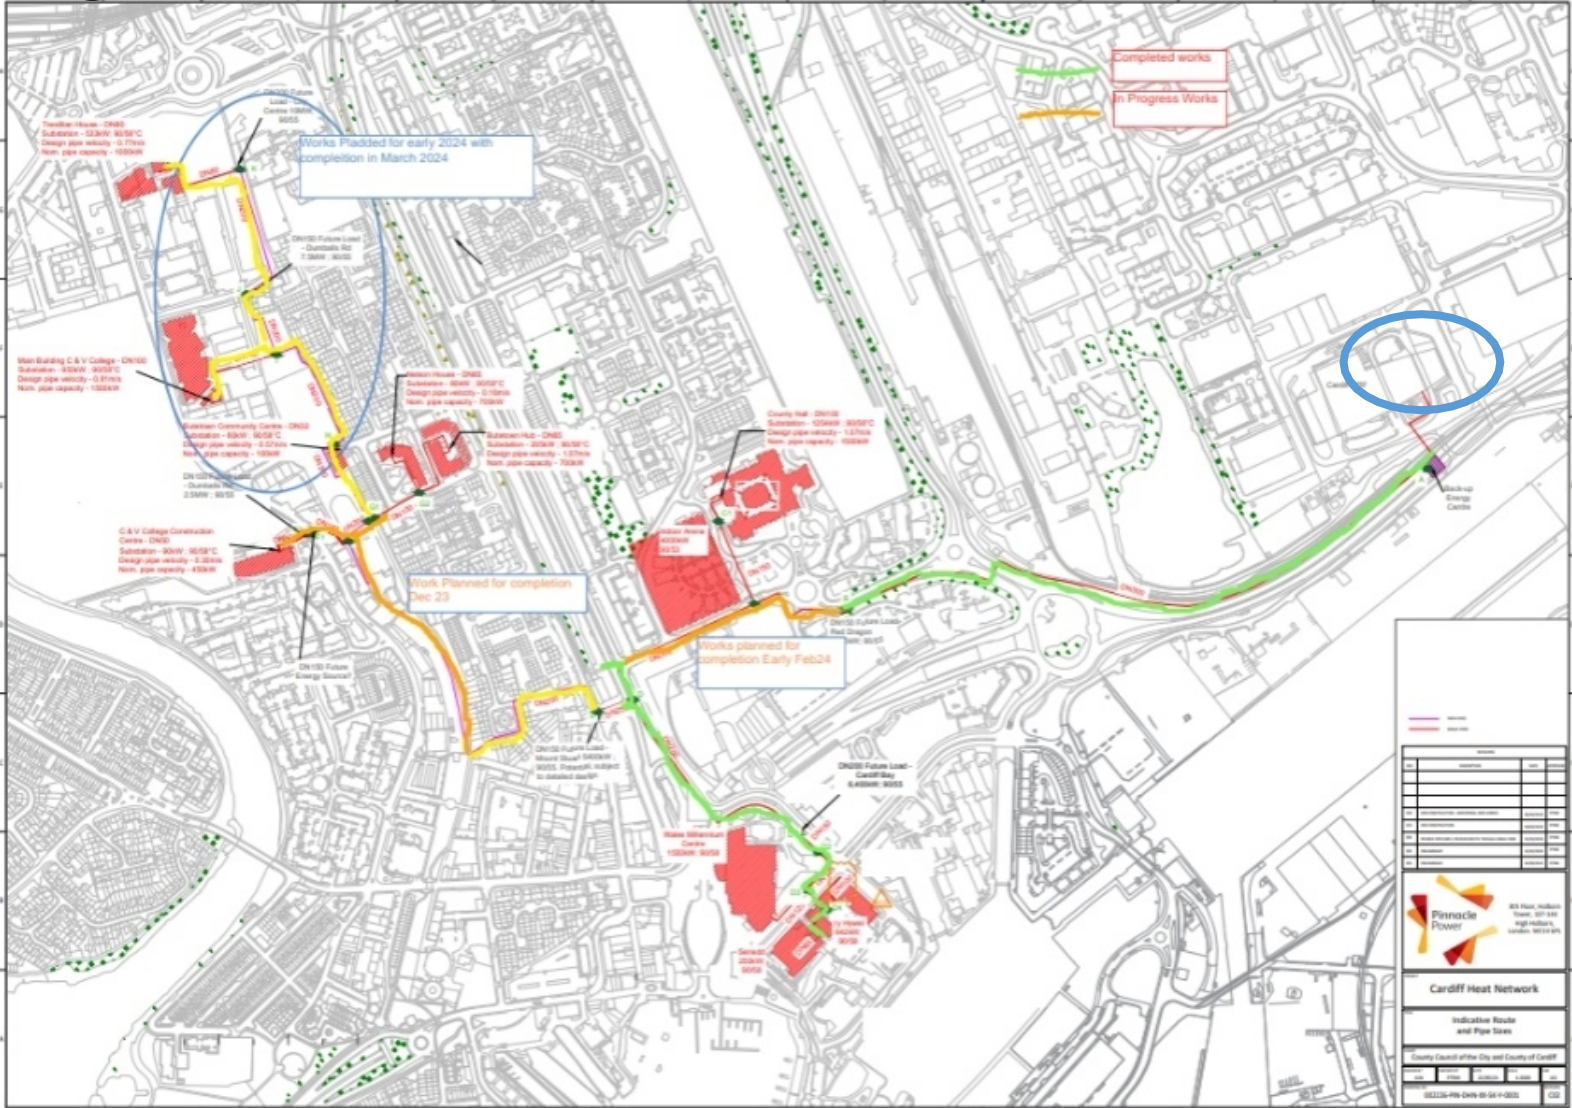

Viridor Works  
Potential Completion  
Delay – Autumn 24

Practical Completion – April/May2024:  
Network  
Energy Centre  
Customer Connections

Gweithio dros Gaerdydd, gweithio gyda'n gilydd  
Working for Cardiff, working together
